




UNDER CONSTRUCTION

Ludington Area Schools MSHS Additions and Renovations




Project Duration is 24% Complete



HS Classroom Polished Concrete



HS Classroom Exterior

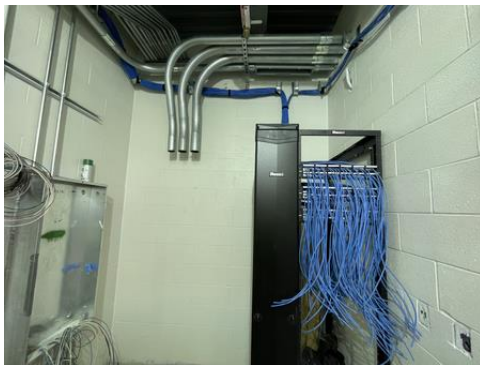

HS Classroom Data / Electrical Room

WORK IN PROGRESS

This Month

- Dry in MS classrooms
- Initial floor grind on MS classrooms
- Measure curtainwall on HS office
- Hang drywall in HS office
- Pave HS student lot
- Install underground water detention tanks / storm piping

Next Month

- Have HS office dried in
- Begin phase IA renovations
- Paint HS office walls
- Continue site work demo, piping, and grading

PROJECT MANAGEMENT UPDATE

Safety

- This month's Safety Goal focuses on safe demolition practices

Schedule

- The project is on schedule


Other Progress

- Oriole field turf starting in 2 weeks
- Receiving construction drawings for team room on May 18




UNDER CONSTRUCTION

Ludington Area Schools MSHS Additions and Renovations



HS Office Framing

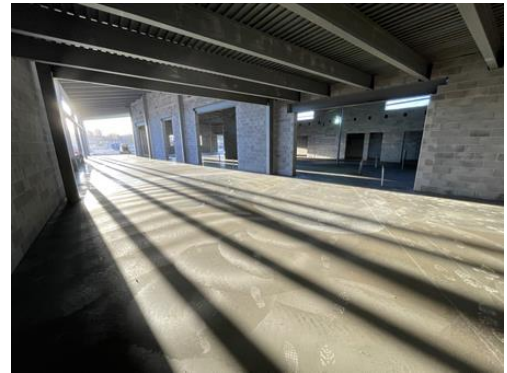

HS Office Floor



HS Office Roof



MS Classroom ERU's



HS Staff Lot Water Detention System



Dewatering for Storm Structures
